



# State Road A1A (State Road 200) six laning Nassau County

Progress update: June 2019

## Project Photo



### Notable Upcoming Impacts

A traffic shift is scheduled for this summer east of the Lofton Creek Bridge. More details will be sent out prior to the traffic shift.

### Job Progress:

The contractor has used 79% of contract time and earned 64% of the contract amount of \$62.2 million. The original contract was 1200 days with 359 days added for additional weather days, holidays and extra work. Completion is scheduled for Winter 2020, depending on weather and unforeseen circumstances.

### Project team members:

Contractor: Superior Construction;

Construction Management Services: England, Thims & Miller (ETM)

Project Owner/Manager: FDOT

## Project status:

### Project limits:

- State Road A1A (State Road 200) from west of Rubin Davis Lane to East of County Road 107/O'Neill Scott Road (4.9 miles)

### Construction activities:

Work began on this \$60 million widening project in early 2016. The 4.9-mile project is the second of a three-phase project to widen A1A from I-95 to O'Neill Scott Road.

Previous construction activities include:

- Continue pond excavation operations
- Phase 2A Westbound roadway drainage installations between Chester Road & Rubin Davis Road
- Phase 2A Westbound roadway ditch construction between Chester Road & Rubin Davis Road
- Phase 2A Westbound roadway base construction between Chester Road & Rubin Davis Road
- Phase 2A Westbound roadway asphalt paving construction between Chester Road & Rubin Davis Road
- Stage 2 bridge demolition (Bent 3)
- Stage 2 bridge cap construction (Bent 1)
- Phase 3 Eastbound roadway drainage installations between Chester Road & Duval Road
- Phase 3 Eastbound roadway embankment construction between Chester Road & Duval Road

Current construction activities include:


- Removals of abandoned water & sewer mains, Chester Road to Rubin Davis Road
- Continue pond excavation operations
- Phase 2A Westbound roadway drainage installations between Chester Road & Rubin Davis Road
- Phase 2A Westbound roadway base construction between Chester Road & Rubin Davis Road
- Phase 2A Westbound roadway asphalt paving construction between Chester Road & Rubin Davis Road
- Stage 2 bridge demolition & pile driving (Bents 3 & 4)
- Stage 2 bridge cap (Bents 3 & 4) construction
- Phase 3 Eastbound roadway drainage installations between Chester Road & Duval Road
- Phase 3 Eastbound roadway embankment construction between Chester Road & Duval Road
- Drilled Shaft installations for signal mast arms
- Phase 3 Chester Road drainage installations between Chester Road & Duval Road
- Phase 3 Chester Road widening, utility adjustments



# State Road A1A (State Road 200) six laning Nassau County

Progress update: June 2019

## Project Photo

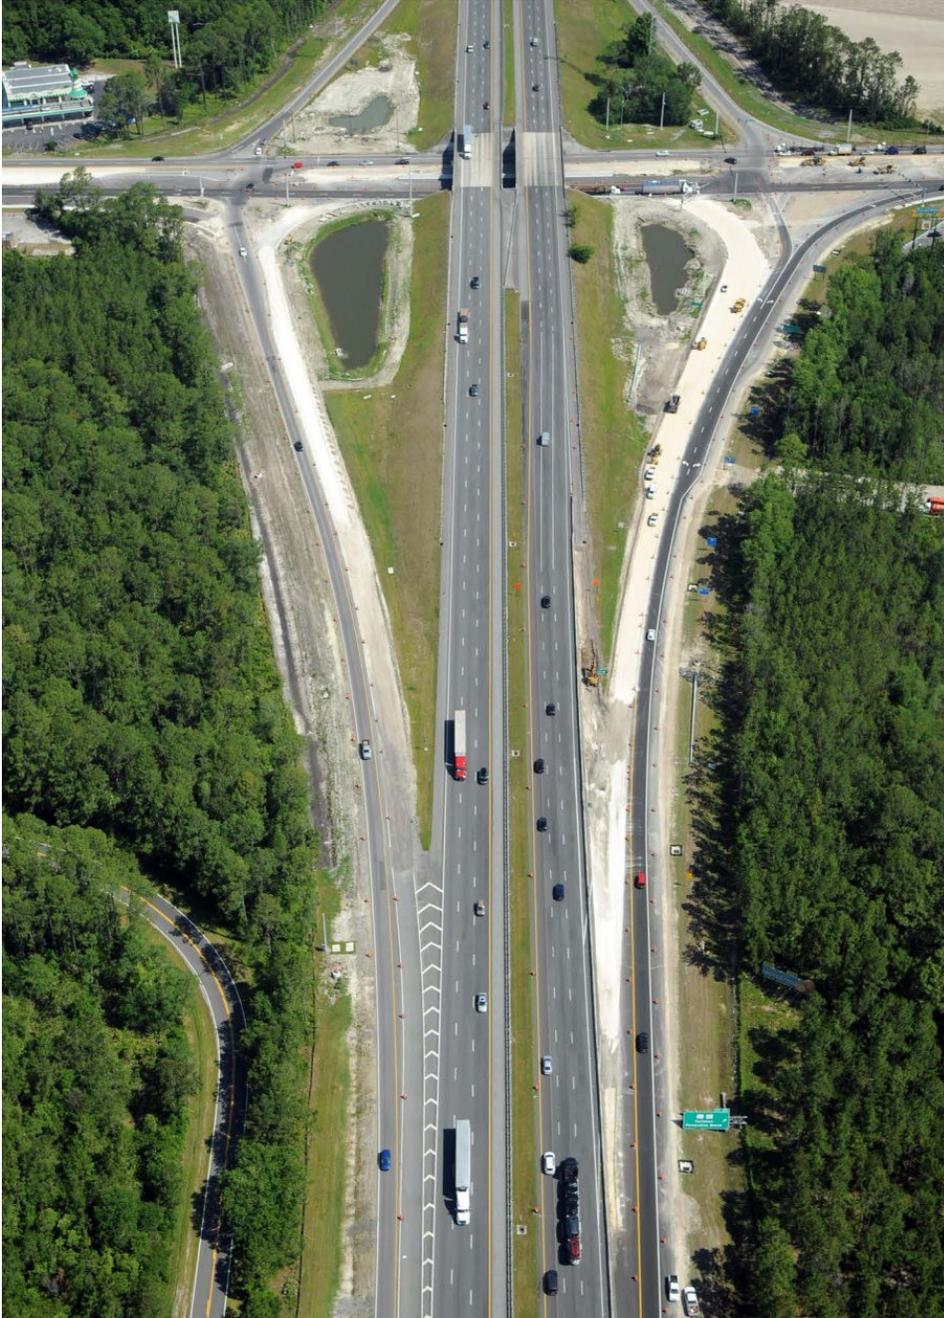

### Job Progress:

The contractor has used 65% of contract time and earned 62% of the contract amount of \$41 million. The original contract is 1040 days with 314 days added for additional weather days, holidays and extra work. Completion is scheduled for summer 2020, depending on weather and unforeseen circumstances.

## Project status:

### Project limits:

- State Road A1A (State Road 200) from west of Interstate 95 to west of Still Quarters Road

### Construction activities:

Work began on this \$39 million project in January 2017. This project includes construction of the area's first Diverging Diamond Interchange (DDI) at Interstate 95. Plans also include widening the roadway from four lanes to six lanes with raised medians, curb and gutter, sidewalks and bicycle lanes. This project is the third and final project to widen A1A from I-95 to O'Neill Scott Road.

### Previous construction activities include:

- Placing/grading limerock base
- Place concrete sidewalk
- Permanent drainage installation
- Pond/roadway excavation
- Asphalt paving
- Sod installation
- Lane striping for Phase 3
- Signalization
- Eastbound traffic shifted onto permanent pavement

### Current construction activities include:

- Pond/roadway excavation
- Roadway embankment
- Remove existing limerock
- Permanent drainage installation
- Asphalt paving
- Milling existing asphalt

## Project team members:

### Contractor:

J.B. Coxwell Contracting, Inc.

### Construction Management Services:

Eisman and Russo

Project Owner/Manager: FDOT
